

CREATIVE HUB WEBSITE 2025

Iteration 1 Sprint Report Prepared By: Saugat KC

TABLE OF CONTENTS

1. Sprint Overview	3
2. Sprint Goal	. 3
3. Sprint Backlog (User Stories / Tasks)	3
4. Planned vs Completed Work vs Bugs	. 4
5. Team Capacity & Velocity	5
6. Key Deliverables	6
7. Blockers / Issues	6
8. Definition of Done (DoD)	. 6
9. Retrospective Insights	. 6
10. Action Items / Next Steps	. 6

1. Sprint Overview

Sprint: Iteration 1

Sprint Start: 2025-08-13 Sprint End: 2025-08-19 Sprint Duration: 1 week

2. Sprint Goal

The goal of this sprint was **to design and develop the entire home page sections** from scratch with all design, development, and backend parts completed.

3. Sprint Backlog (User Stories / Tasks)

Task	Assignee
Coming Soon Development Page	Nirjala Shakya
Home Page Design	Sameer Acharya
Home Page Development	Mandip Shrestha
Logo Animation	Manjil Aryal
Backend Setup	Nirjala Shakya
QA tasks and Documentation	Saugat KC
Understanding the working of Supabase	Mandip Shrestha

4. Planned vs Completed Work vs Bugs

Planned Work: 11 items assigned for Iteration 1. **Completed Work:** 4 items successfully completed.

Bugs: 2 items were found as bugs.

→ Completed Tasks


- 1. Coming Soon Development Page
- 2. Logo Animation
- 3. Hero Section Design
- 4. Home Page About Section Design

→ Carried Over Work

- 1. Home Page History Section Design
- 2. Home Page Teams Section Design
- 3. Hero Section Dev
- 4. Home Page About us Section Dev
- 5. Home Page History Section Dev
- 6. Home Page Teams Section Dev
- 7. Home Page About Section Dev

→ Bugs and Issues

- 8. Major Deployment Issue
- 9. Favicon issue

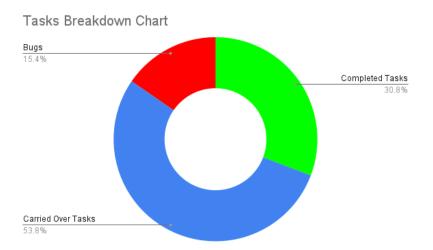


5. Team Capacity & Velocity

Planned: 13 items **Completed:** 4 items

Team Velocity for this sprint: ~30% completion rate.



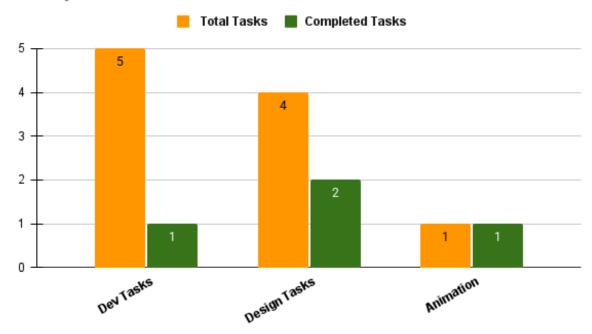

6. Key Deliverables

- 1. Coming Soon Development Page
- 2. Logo Animation
- 3. Hero Section Design
- 4. Home Page About Section Design

7. Blockers / Issues

- 1. Overestimation of tasks within the sprint capacity.
- 2. Limited resources available for backend and development.
- 3. Deployment challenges impacted progress.
- 4. SEO and favicon-related issues required extra attention.

8. Definition of Done (DoD)

- 1. Design meets agreed acceptance criteria.
- 2. Code is implemented, reviewed, and tested.
- 3. Features are integrated into the system without breaking existing functionality.
- 4. Deployed successfully in the test environment.
- 5. QA signoff received for the deployed codes.
- 6. Documentation updated where applicable.

9. Retrospective Insights

- 1. Need to improve estimation practices to better match team capacity.
- 2. Earlier identification of resource constraints is required.

10. Action Items / Next Steps

- 1. Work on MVP and hold the proposed fullstack system.
- 2. Ensure SEO and metadata issues are addressed during development.
